

# Product Roadmap & Demo Strategy

A feasible eight-month path from thirteen working prototypes to one federated creative operating system — and the eighteen-minute demonstration that proves it at week ten.

**The strategic finding.** ANCR's defensible asset is not any one of its thirteen applications. It is the **single verified creator record** that accumulates across all of them and cannot be forged. The roadmap must therefore sequence **federation before features** — and the demo must show one record travelling, not thirteen products sitting still.

## 01 Executive summary

---

Thirteen applications are built and running. None of them are yet a platform. The gap is not features — it is federation, and it is closeable in ten weeks for the demo and eight months for production.

**13**

### APPLICATIONS BUILT

React · FastAPI · MongoDB.  
All with seeded data and  
working UIs.

**1 of 9**

### SSO CLIENTS WIRED

ANCRID issues tokens for  
nine registered clients. Zero  
consumers verify them.

**0**

### LIVE CROSS-PRODUCT EVENTS

No event spine running. All  
cross-module data is  
seeded or same-database.

**10 wks**

### TO A CREDIBLE DEMO

Phase 0 + Phase 1 + a  
three-event slice of Phase  
2.

### What the audit found

The repository contains an unusually complete product estate. Every one of the thirteen applications has a real backend, real routes, real seed data and a designed front end. The specifications are thorough and mostly internally consistent. This is **substantially more built product than a company at this stage normally has**, and that is the asset to protect.

It also found that the applications are **thirteen independent prototypes, not one system**. Each maintains its own users, its own JWTs and its own database. ANCRID exposes a working SSO service at `/api/sso/authorize` with nine registered clients — and not one of the nine actually verifies an ANCRID token today. ANCRLaunch simulates its ecosystem providers by reading collections prefixed `ancra_`, `ancrid_` and `ancrLab_` out of its own Mongo instance. The persona "Maya Ellis" is seeded independently in at least six modules, with a different identifier in each.

### THE CONSEQUENCE FOR A DEMO

A tour of thirteen applications proves that thirteen applications exist. It does not prove a platform, and a technically literate evaluator will identify the seams inside five minutes — different logins, different identifiers for the same person, data that could not have travelled. **The tour format actively works against the thesis.**

### The recommendation, in three sentences


**One.** Spend two weeks on decisions before any code — the estate contains two products named "Passport", a folder called `ANCR-ANCRSYNC-` that is actually ANCRLaunch, and two competing commerce systems. Cheap to fix now; expensive once deployment automation exists.

**Two.** Make identity real before making anything else real. One `ancrid` present in all thirteen databases and three products genuinely verifying ANCRID tokens converts the estate from a portfolio into a platform, and it is roughly six weeks of work.

**Three.** Demonstrate at week ten, on the narrowest possible path — one creator, one song, five applications, one live event chain. Everything else is a map on a slide.

## 02 Where the product actually stands

The estate is deep on domain logic and shallow on federation. Every application solves its own problem well; almost none of them can talk to another one.

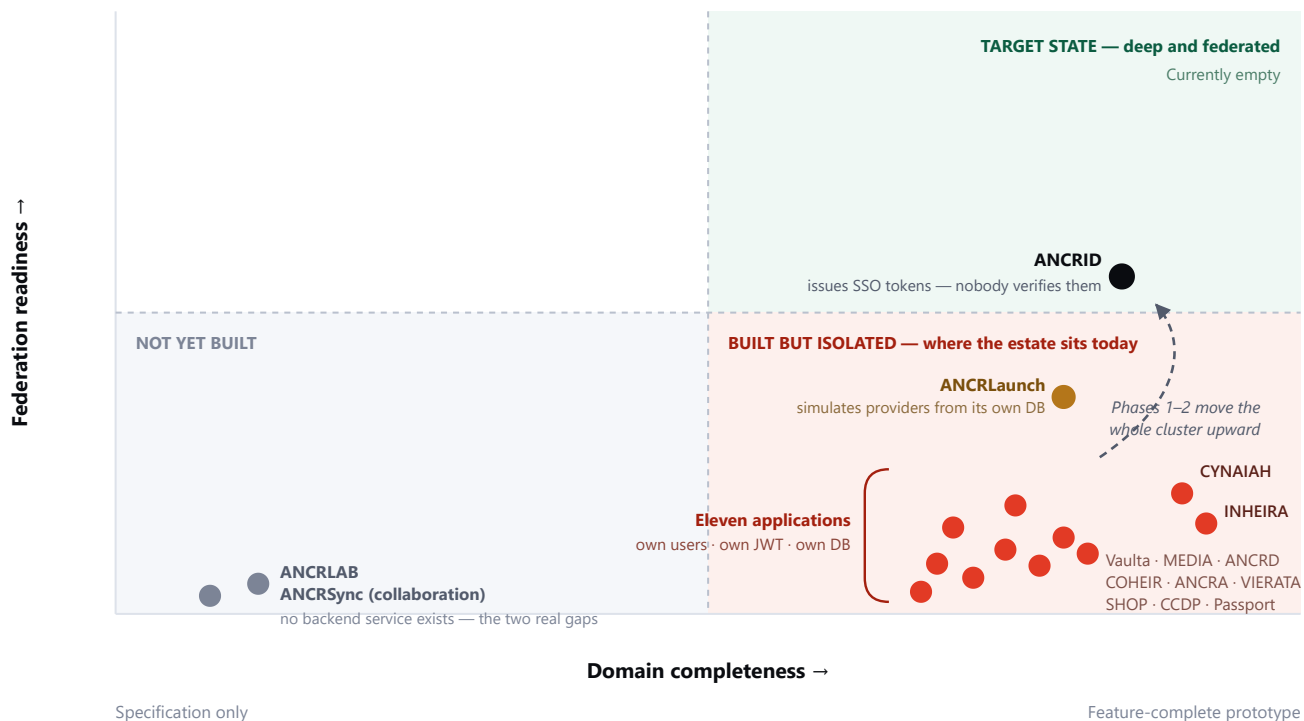

**Figure 1 — Portfolio maturity.** Position is derived from the code audit: horizontal axis from implemented routes, models and UI surface; vertical axis from whether the application accepts external identity, publishes domain events, or reads canonical records over a contract. The estate's problem is entirely vertical. Building more features moves applications right, which is the axis that is already won.

## What this means for sequencing

Because the horizontal axis is largely won, **feature work has low marginal value right now** and federation work has extremely high marginal value. Two applications — ANCR LAB and the real ANCR Sync collaboration service — sit in the bottom-left and need building outright, but they should be built **after** contracts exist so they are built once, against the finished interface, rather than twice.

## 03 Seven decisions that gate the roadmap

Governance decisions, not engineering tasks. None require code; all get more expensive every week they stay open, and three will visibly damage a demo if an evaluator finds them live.

| #  | OPEN CONFLICT                                                                                                                                                 | RECOMMENDED RESOLUTION                                                                                                                                                                                                       | COST OF LEAVING IT OPEN                                                                                          | OWNER / EFFORT                   |
|----|---------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------|----------------------------------|
| D1 | <b>ANCRSync vs ANCRLaunch.</b> The folder ANCR-ANCRSYNC- contains the career-placement product, not the collaboration product.                                | Rename the repository to ANCR-ANCRLAUNCH and create a separate home for the real ANCRSync collaboration service — before any deployment automation, CI or DNS attaches to the current name.                                  | <b>DEMO-VISIBLE</b> An evaluator who opens the repo or reads a URL sees the contradiction immediately.           | Eng lead<br>½ day                |
| D2 | <b>Two meanings of "Passport".</b> Creator Passport (ANCRID's verified professional record) and ANCR Passport (study-abroad product).                         | Never use the bare word. Enforce <b>Creator Passport™</b> and <b>ANCR Passport™</b> in every UI string, route, API field and document. Add a lint rule.                                                                      | <b>DEMO-VISIBLE</b> The single most likely source of confusion in a live walkthrough.                            | Product<br>1 day                 |
| D3 | <b>Two commerce systems.</b> CCDP Web and ANCRSHOP both implement customers, catalog, checkout and orders.                                                    | Name ANCRSHOP the commerce system of record and reduce CCDP Web's store to a presentation layer that calls it. Migrate CCDP orders once, before either has real volume.                                                      | <b>DIVERGENCE</b> Duplicated customers, inventory and orders that will not reconcile later.                      | Product + Eng<br>1 day to decide |
| D4 | <b>ANCRA's role.</b> One INHEIRA-era document redefines ANCRA as the analytics and event-bus layer; current spec and code define it as the learning platform. | ANCRA stays the learning operating system. Name the transport neutrally — <b>ANCR Event Spine</b> — so infrastructure is never confused with a product.                                                                      | <b>ARCHITECTURE DRIFT</b> Engineers building against the wrong canonical document.                               | CTO<br>½ day                     |
| D5 | <b>COHEIR's domain.</b> Current spec says mentorship; an older architecture assigns estate and heir-succession duties.                                        | COHEIR is mentorship only. Rights succession belongs to INHEIRA; financial and estate execution belongs to Vaulta, subject to legal design.                                                                                  | <b>SCOPE CREEP</b> A sensitive legal domain landing in the wrong system.                                         | CTO + Legal<br>½ day             |
| D6 | <b>Ten core modules vs thirteen applications.</b> CYNIAH, ANCR Passport, VIERATA and ANCRSHOP sit outside the canonical ten.                                  | Publish them as <b>vertical experiences and platform extensions</b> — first-class products that consume core contracts but are not additional systems of record.                                                             | <b>NARRATIVE RISK</b> "What is the actual product?" is the hardest question to answer with thirteen equal tiles. | Product<br>1 day                 |
| D7 | <b>Superseded architecture documents.</b> Multiple generations of "canonical" specs coexist in the repository.                                                | Stamp every superseded document <b>SUPERSEDED BY ...</b> on page one. Publish a single module registry — name, slug, owner, URL, API audience, canonical entities, status — as the one index engineers are allowed to trust. | <b>REWORK</b> Every new engineer picks a different document and builds the wrong thing.                          | CTO<br>2 days                    |

### TOTAL COST OF PHASE 0 — AND WHY IT COMES FIRST

Roughly **six person-days of decisions** over a two-week window. The cheapest phase in the roadmap, and it unblocks every subsequent one. No code is written.

Every decision above changes a name, a boundary or an owner — and names and boundaries get embedded into route paths, database collections, deployment pipelines, DNS records, JWT audiences and documentation. Resolving them now costs six days; after Phase 2 it costs a migration for every affected service; after Phase 4, a migration plus a coordinated release across thirteen applications.


## Phase 0's single deliverable — the module registry

The decisions above are only durable if they land in one machine-readable place. The registry is the artefact every later phase reads from: the launcher renders from it, the SSO client list is generated from it, and the event schema registry validates publisher names against it.

| FIELD              | EXAMPLE                  | WHY IT IS IN THE REGISTRY                                                                                                                                                       |
|--------------------|--------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| slug               | ancrlaunch               | The one canonical identifier. Resolves D1 permanently — folder names, repository names and route prefixes all derive from it rather than from each other.                       |
| name               | ANCRLaunch™              | The only string permitted in UI copy. Enforcing <b>Creator Passport</b> and <b>ANCRLaunch Passport</b> as distinct entries here is what makes D2 lintable.                      |
| owner              | Career & placement       | The team accountable for the canonical records. One owner per record is the rule D3–D5 exist to establish.                                                                      |
| tier               | core / extension         | Resolves D6. Determines whether a product is a system of record or a vertical experience consuming core contracts.                                                              |
| api_audience       | ancrlaunch               | The JWT <code>aud</code> claim ANCRID issues for this client. Phase 1 generates the SSO client registry directly from this field rather than from a hand-maintained dictionary. |
| canonical_entities | [application, placement] | What this product is authoritative for. Phase 2 validates that no event publisher claims an entity it does not own.                                                             |
| status             | built / spec             | Distinguishes shipped products from roadmap items, so the launcher and the demo map never present ANCRLAB as clickable.                                                         |
| supersedes         | [doc ids]                | Resolves D7. Any specification not referenced by a current registry entry is superseded by definition.                                                                          |

## 04 The feasible roadmap

Eight months to a genuinely federated platform, with a defensible demonstration available at week ten. Phases overlap where dependencies allow; the critical path runs through identity and contracts only.

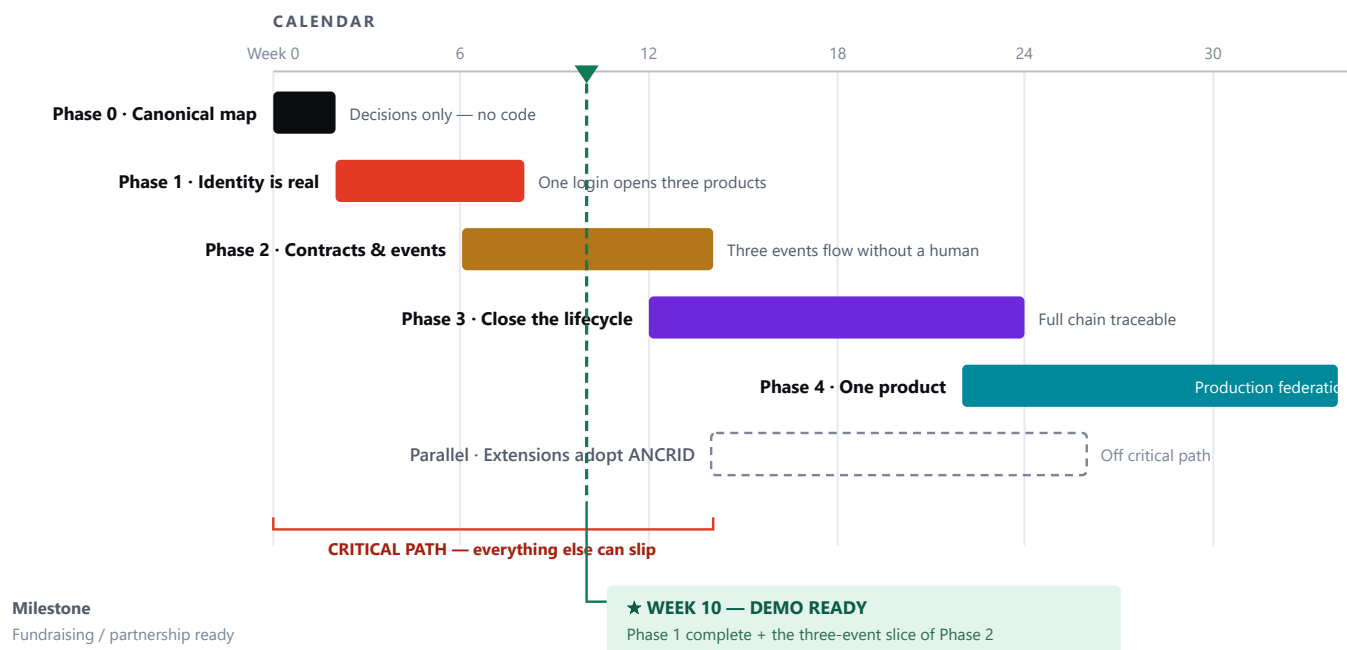

**Figure 2 — Eight-month roadmap.** Estimates assume three full-stack engineers and one designer working the critical path, with extension products maintained in parallel by their existing owners. Phases 1 and 2 overlap deliberately: contract design can begin as soon as the identity model is fixed, and the demo depends on a thin slice of Phase 2 landing early.

### Sequencing logic

The roadmap is ordered by **what unblocks the most downstream work per unit of effort**, not by product priority. Identity unblocks everything, so it is first. Contracts unblock all cross-product data movement, so they are second. Only then is it worth building the missing services — ANCRILAB's asset backend and the real ANCRSync collaboration service — because building them before contracts exist means building them twice.

The demo sits deliberately at the **end of Phase 1 plus a thin slice of Phase 2** — early enough to be useful for fundraising and partnership conversations, late enough that nothing on stage has to be faked.

### The two facts that make this feasible

**The hard part is already built.** Thirteen working backends with real domain models is normally the multi-year cost of a platform like this. What remains is integration work, which is bounded, well-understood and does not require product discovery.

**ANCRID's SSO service already exists and works.** It issues audience-scoped, five-minute JWTs for nine registered clients and exposes a verification endpoint. Phase 1 is not "build SSO" — it is "wire consumers to the SSO that is already running," which is a substantially smaller and more predictable job.

## 05 Phase detail & exit criteria

A phase is complete when its exit criterion can be demonstrated, not when its tickets are closed. Each criterion below is written as something a sceptical observer can watch happen.

### Phase 1 · Identity is real WEEKS 2–8 · CRITICAL PATH

Converts the estate from thirteen products into one platform. This is the highest-leverage work in the entire roadmap and the phase the demo depends on.

| WORKSTREAM                     | SCOPE                                                                                                                                                                                                                                    | EFFORT         | DEPENDS ON |
|--------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------|------------|
| 1.1 Canonical ANCRID backfill  | Assign one permanent <code>ancrid</code> to every seeded persona and write it into all thirteen module databases. Maya Ellis must carry an identical identifier in ANCRA, INHEIRA, Vaulta, ANCRMEDIA, COHEIR, CYNIAAH and ANCR Passport. | 6 days         | D1, D2     |
| 1.2 Token verification library | One shared Python package that verifies an ANCRID token and yields a request principal. Published once, imported by every FastAPI service. Replaces per-module JWT logic.                                                                | 5 days         | —          |
| 1.3 Wire three consumers       | INHEIRA, Vaulta and ANCRMEDIA accept ANCRID tokens for real. Local password storage is removed from those three. The remaining ten keep local auth until Phase 3.                                                                        | 9 days         | 1.1, 1.2   |
| 1.4 OIDC / JWKS upgrade        | Move ANCRID from shared-secret HS256 to RS256 with a published JWKS endpoint, so consumers verify without holding a secret. Keep the existing demo path working during transition.                                                       | 6 days         | 1.2        |
| 1.5 Ecosystem launcher         | A shared app-switcher component rendered in every module's chrome, driven by the module registry. Pure front end; the single cheapest change that makes thirteen applications feel like one.                                             | 5 days         | D7         |
| 1.6 Consent & revocation       | Centralise grant records in ANCRID; revoking a grant blocks the next token issue. Full propagation is Phase 4; revocation-at-issue is enough here.                                                                                       | 4 days         | 1.3        |
| Phase 1 total                  | <b>One login, one identifier, one launcher, three federated products</b>                                                                                                                                                                 | <b>35 days</b> |            |

#### EXIT CRITERION

A single login at ANCRID opens INHEIRA, Vaulta and ANCRMEDIA in new tabs with no second authentication, and the same `ancrid` string is visible on screen in all four applications. Revoking the grant in ANCRID prevents the next launch.

### Phase 2 · Contracts & the first three events WEEKS 6–14 · CRITICAL PATH

Cross-product data stops being seeded and starts being **transmitted**. Deliberately narrow: three events, not a catalogue.

| WORKSTREAM              | SCOPE                                                                                                                                                                                                                                                                                                   | EFFORT  | DEPENDS ON |
|-------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------|------------|
| 2.1 Schema registry     | JSON Schemas for the canonical IDs and the event envelope — <code>schema_version</code> , <code>event_id</code> , <code>occurred_at</code> , <code>actor_ancrid</code> , <code>subject_ref</code> , <code>correlation_id</code> , <code>idempotency_key</code> . A versioned repository, not a service. | 5 days  | D4, D7     |
| 2.2 Outbox pattern      | An outbox collection in each publishing product so a domain write and its event publication cannot diverge. Implemented in INHEIRA, ANCRMEDIA and Vaulta first.                                                                                                                                         | 8 days  | 2.1        |
| 2.3 Event Spine — thin  | A minimal relay draining outboxes to subscriber webhooks with retry and a dead-letter collection. <b>Do not deploy NATS JetStream yet.</b> The interface is what matters; the transport can be swapped in Phase 4 without touching producers.                                                           | 9 days  | 2.2        |
| 2.4 The three flows     | <code>rights.splits_approved.v1</code> (INHEIRA → ANCRMEDIA, Vaulta) · <code>media.release_published.v1</code> (ANCRMEDIA → Vaulta, ANCRD) · <code>finance.royalty_accrued.v1</code> (Vaulta → creator dashboards). Consumers must be idempotent.                                                       | 12 days | 2.3        |
| 2.5 Correlation tracing | Propagate one correlation ID from user action through every event and projection. Surfaced as a readable trace view — this doubles as a demo asset.                                                                                                                                                     | 5 days  | 2.4        |
| Phase 2 total           | Contracts published, three flows live, traceable end to end                                                                                                                                                                                                                                             | 39 days |            |

#### EXIT CRITERION

A split sheet approved by a human in INHEIRA causes a royalty channel to appear in Vaulta and a release record in ANCRMEDIA, with no operator action and no shared database read. Replaying the same event twice produces no duplicate records.



## 05 Phase detail & exit criteria (continued)

### Phase 3 · Close the lifecycle WEEKS 12–24

Builds the two genuinely missing services and removes the last simulated integrations. Off the demo's critical path — this is the work that makes the demo's promises true in production.

| WORKSTREAM                                | SCOPE                                                                                                                                                                                                                   | EFFORT         | DEPENDS ON  |
|-------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------|-------------|
| <b>3.1 ANCRLAB asset service</b>          | The standalone backend that does not exist today: room bookings, project and session records, stem and master versioning, export pipeline, signed-URL object storage. Publishes <code>creative.master_ready.v1</code> . | 30 days        | 2.1–2.3     |
| <b>3.2 ANCRSync collaboration service</b> | The real collaboration product: workspaces, teams, writing rooms, shared sessions, collaboration history. Publishes <code>collaboration.credit_proposed.v1</code> into INHEIRA.                                         | 28 days        | D1, 2.1–2.3 |
| <b>3.3 De-simulate ANCRLaunch</b>         | Replace the same-database <code>SeededProvider</code> classes with live HTTP providers and event projections. The code is already written to allow this swap without touching the application.                          | 10 days        | 1.3, 2.4    |
| <b>3.4 Evidence into readiness</b>        | COHEIR reviews and ANCRD reputation feed ANCRLaunch readiness as projections — never as copied authoritative records.                                                                                                   | 9 days         | 3.3         |
| <b>3.5 Remaining ANCRID adoption</b>      | ANCRA, COHEIR, ANCRD and CYNIAH move to ANCRID tokens. Extensions (VIERATA, ANCR Passport, ANCRSHOP) follow on the parallel track.                                                                                      | 14 days        | 1.4         |
| <b>Phase 3 total</b>                      | <b>Every lifecycle stage owned by a real service</b>                                                                                                                                                                    | <b>91 days</b> |             |

#### EXIT CRITERION

A learning assignment in ANCRA can be traced by a single correlation chain through creation, collaboration, rights, release, royalty and career readiness — with each hop served by a distinct service over a published contract.

### Phase 4 · One product WEEKS 22–34

| WORKSTREAM                          | SCOPE                                                                                                                                                          | EFFORT  | DEPENDS ON |
|-------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------|---------|------------|
| <b>4.1 @ancr/ui design system</b>   | Shared component library and tokens. Every product keeps its accent identity but shares account, notification, consent and app-switching behaviour.            | 22 days | 1.5        |
| <b>4.2 AIAH tool gateway</b>        | Permission-scoped tools over product APIs with a complete audit trail. AIAH must never bypass domain validation or silently write legal or financial outcomes. | 18 days | 1.6, 2.4   |
| <b>4.3 Event Spine — production</b> | Swap the thin relay for NATS JetStream with dead-letter handling and idempotency tracking. Producers and consumers unchanged.                                  | 10 days | 2.3        |


| WORKSTREAM                           | SCOPE                                                                                                                                  | EFFORT         | DEPENDS ON |
|--------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|----------------|------------|
| <b>4.4 Observability &amp; audit</b> | Central structured logs, traces and an audit trail answering "which person or service changed this record" for every canonical entity. | 12 days        | 2.5        |
| <b>4.5 Consent propagation</b>       | Revoking identity or consent in ANCRID propagates to every product within seconds, not at next login.                                  | 8 days         | 1.6, 4.3   |
| <b>Phase 4 total</b>                 | <b>The eight interconnection tests pass</b>                                                                                            | <b>70 days</b> |            |

## ROADMAP TOTALS

| PHASE                         | CALENDAR         | ENGINEERING DAYS | STRATEGIC RESULT                            |
|-------------------------------|------------------|------------------|---------------------------------------------|
| Phase 0 · Canonical map       | Weeks 0–2        | 6                | One agreed map; naming landmines defused    |
| Phase 1 · Identity is real    | Weeks 2–8        | 35               | <b>Portfolio becomes a platform</b>         |
| Phase 2 · Contracts & events  | Weeks 6–14       | 39               | Data moves by contract, not by seeding      |
| Phase 3 · Close the lifecycle | Weeks 12–24      | 91               | Every stage owned by a real service         |
| Phase 4 · One product         | Weeks 22–34      | 70               | Production-grade federation                 |
| <b>Total</b>                  | <b>~34 weeks</b> | <b>241 days</b>  | <b>≈ 3 engineers + 1 designer, 8 months</b> |

## 06 The demo thesis — the Golden Thread

Do not tour thirteen applications. Follow one creator, one song and one identifier through five of them, and let the map do the work for the other eight.

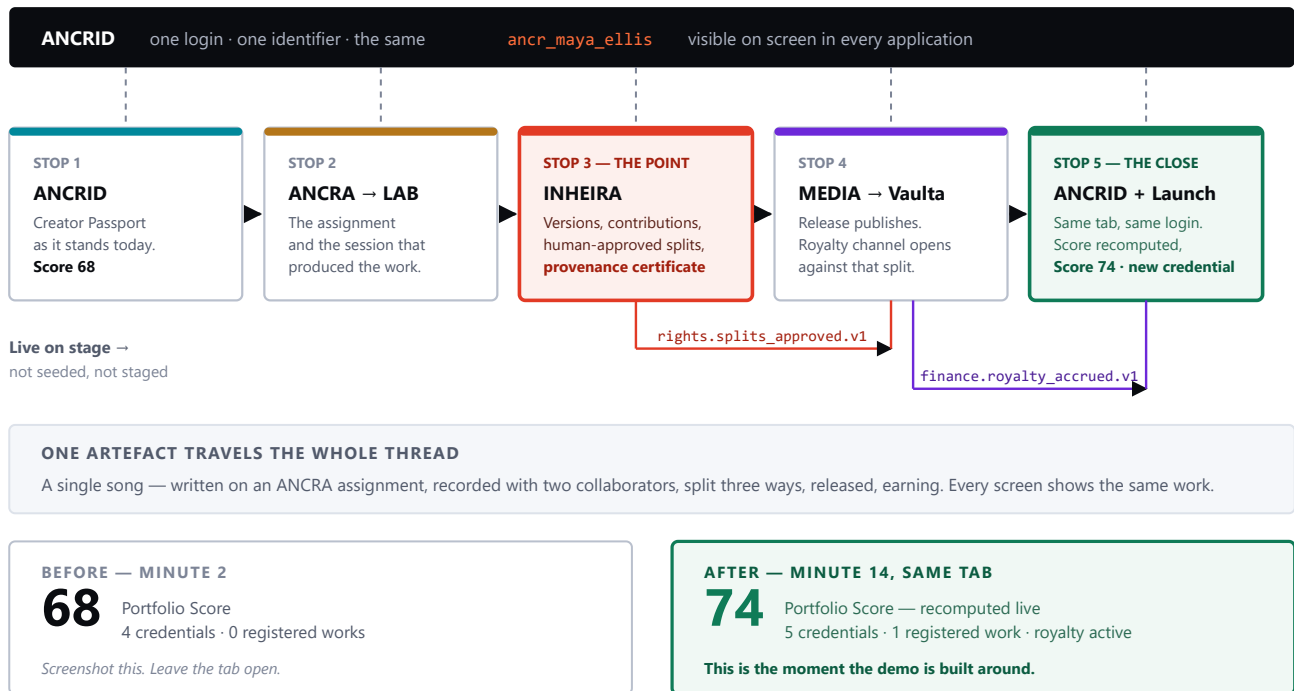

**Figure 3 — The Golden Thread.** Five applications, one identifier, one artefact, one closed loop. Stop 3 carries the competitive claim — provable human authorship in an era where authorship is contested. Stop 5 carries the platform claim — that verified creative work compounds into career standing without anyone re-entering it.

### Why this format and not a tour

A tour answers “what did you build?” The Golden Thread answers “**why does this have to be one system?**” — which is the only question that justifies thirteen applications instead of one. Every stop on the thread is impossible without the previous stop, and that dependency is the argument.

It also fails safely. If an application on the thread misbehaves, the narrative survives, because the audience is following a story about a creator rather than an inventory of screens.

#### THE ONE QUESTION TO PREPARE FOR

**“Is this real, or is it seeded?”** The honest answer at week ten is: identity and the three-event chain are real and happening live; the surrounding records are seeded demonstration data. Say it plainly and then prove the real part — open the trace view and show the correlation ID crossing service boundaries. Volunteering the boundary buys more credibility than any screen in the demo.

07 Demo scope — what is clicked, shown and hidden

Three tiers. The discipline is in tier three: an application that is not on the thread must not be opened, however good it looks.


| TIER                                   | APPLICATIONS                                                                                              | TREATMENT AND REASONING                                                                                                                                                                                                                                                                                    |
|----------------------------------------|-----------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <div>CLICKED</div> <div>5 apps</div>   | <b>ANCRID · ANCRA</b> (or CYNIAIAH for a visual story) · <b>INHEIRA · ANCRMEDIA → Vaulta · ANCRLaunch</b> | Driven live, in one browser profile, in this order. Each earns its place by being a link in the causal chain — remove any one and the story breaks. Five is the ceiling: beyond that the audience stops tracking the thread and starts counting screens.                                                   |
| <div>SHOWN</div> <div>4 apps</div>     | <b>COHEIR · ANCRD · ANCRLAB · ANCRSync</b>                                                                | One architecture slide with real screenshots, thirty seconds total. COHEIR and ANCRD are built but off-thread; ANCRLAB and ANCRSync are honest roadmap items. Presenting all four the same way is the correct move — the audience learns the shape of the platform without being invited to open anything. |
| <div>HELD BACK</div> <div>4 apps</div> | <b>CYNIAIAH</b> (if not chosen at stop 2) · <b>VIERATA · ANCR Passport · ANCRSHOP / CCDP store</b>        | Genuinely strong products that are off-thesis for this demonstration. Holding them back is not hiding weakness — it is the strongest available signal that the company knows what its product is. Offer them explicitly as a follow-up session; that offer lands better than an unplanned detour.          |

THE RULE THAT PROTECTS THE DEMO

When asked “can we see the wellness one?” mid-thread, the answer is “**yes — right after we close the loop, so you can see where its data lands.**” This defers without deflecting, and it re-frames the extension product as part of the same system rather than a separate demo.

08 Demo build backlog

Fifty-one engineering days of demo-specific work, all of which is Phase 1 and Phase 2 roadmap work rather than throwaway. Nothing here is built only for the stage.

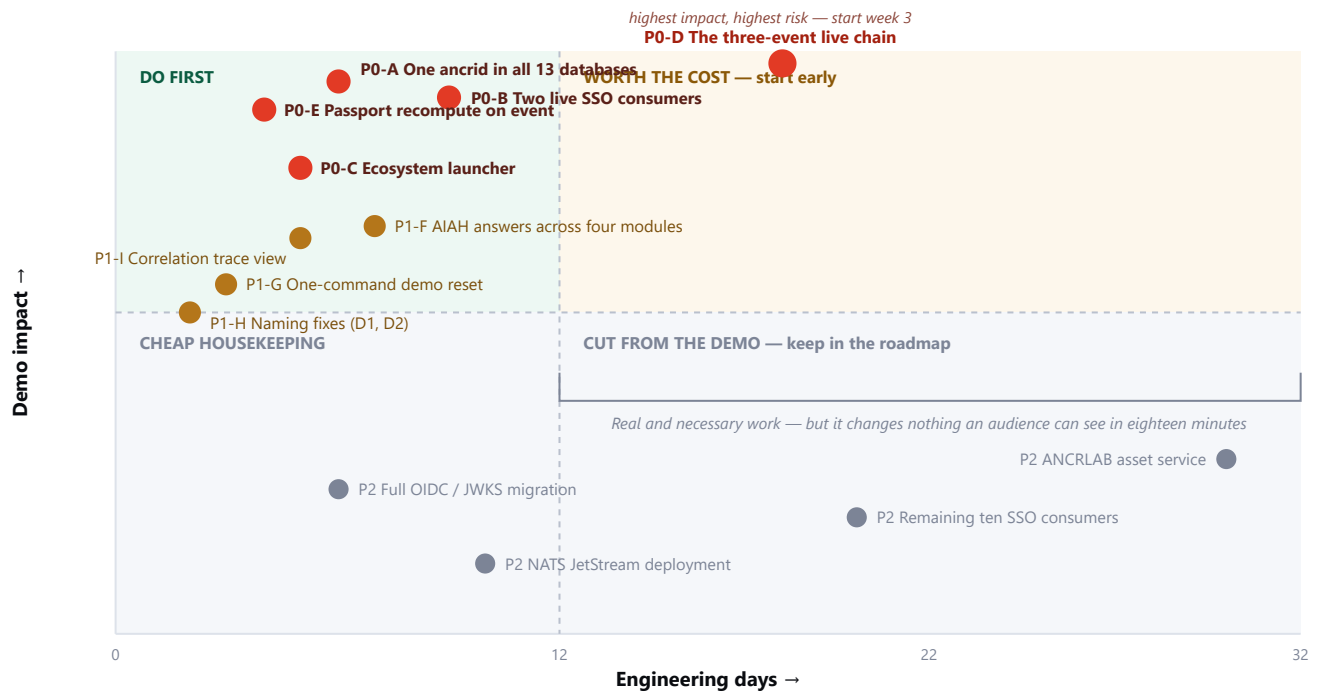

**Figure 4 — Demo build backlog by effort and impact.** Impact is scored as “how much of the platform thesis collapses if this is absent on stage.” The four items in the lower-right quadrant are correctly prioritised in the production roadmap and correctly excluded from the demo build — deploying NATS before the demo would consume ten days and change nothing the audience experiences.

## 08 Demo build backlog (detail)

| ID               | ITEM                                                  | WHAT IT DELIVERS ON STAGE                                                                                                                                                                                                                 | DAYS      | ROADMAP HOME                     |
|------------------|-------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------|----------------------------------|
| P0-A             | One <code>ancrid</code> across all thirteen databases | Maya's identifier reads identically in every application. This is the first thing a technical evaluator checks and the cheapest way to fail if it is wrong.                                                                               | 6         | Phase 1.1                        |
| P0-B             | Two consumers genuinely verifying ANCRID tokens       | A real, unfaked single sign-on handoff performed live. Two proves the pattern; the launcher implies the remaining eleven. Wiring all thirteen before the demo would cost three extra weeks and add nothing to the argument.               | 9         | Phase 1.3                        |
| P0-C             | Ecosystem launcher in every module chrome             | The single cheapest change that makes thirteen applications read as one product. Front-end only.                                                                                                                                          | 5         | Phase 1.5                        |
| P0-D             | Three-event chain, live                               | <b>The centrepiece.</b> A split approved on stage causes a release record and a royalty channel to appear in two other applications, unaided. Everything else in the demo is a screen; this is the only moment the platform <b>acts</b> . | 18        | Phase 2.2–2.4                    |
| P0-E             | Creator Passport recompute on event                   | The before/after score movement in the same browser tab. Small change, largest emotional payload in the session.                                                                                                                          | 4         | Phase 1.1 + 2.4                  |
| P1-F             | One AIAH cross-module answer                          | "Is Maya ready to graduate?" answered with visible citations drawn from four modules. Distinguishes an intelligence layer from a chatbot. Scope to <b>one</b> rehearsed question.                                                         | 7         | Phase 4.2 (pulled forward, thin) |
| P1-I             | Correlation trace view                                | The proof artefact for "is this real?" — one ID crossing service boundaries, readable on screen.                                                                                                                                          | 5         | Phase 2.5                        |
| P1-G             | One-command demo reset                                | Restores every database to the pre-demo snapshot in under a minute. Non-negotiable the moment the demo is given more than once, and the reason most repeat demos degrade.                                                                 | 3         | Demo infrastructure              |
| P1-H             | Naming fixes shipped to the UI                        | Removes the two visible contradictions (D1, D2) from every screen the audience sees.                                                                                                                                                      | 2         | Phase 0                          |
| Demo build total |                                                       | <b>All of it is roadmap work brought forward — none of it is discarded after the demo</b>                                                                                                                                                 | <b>59</b> |                                  |

### SCHEDULING NOTE

Fifty-nine days across three engineers is roughly four calendar weeks of parallel work, which fits inside the weeks 3–10 window with slack. **Start P0-D in week 3**, not week 7 — it is the only item with genuine technical uncertainty, and it is the one item whose absence would force the demo to be staged rather than live.

09 Run of show — eighteen minutes

Eighteen minutes because the decisive material fits in eighteen minutes and a thirty-minute version invites the tour. Reserve the remaining time for questions, which is where the deal moves.



Figure 5 — Session timeline. Stop 3 is given twice the time of any other stop because it carries the competitive claim. The two dashed markers are the only two moments that must not be rushed or narrated over.

Beat sheet

| TIME  | BEAT             | WHAT IS SAID AND SHOWN                                                                                                                                                                                                                                                        |
|-------|------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 0:00  | Frame            | No screens. One claim: a creator's record of what they made, who they made it with and what they are owed is scattered across a dozen systems that do not talk, and in an era of synthetic work, unverifiable. Name the thesis before showing anything.                       |
| 2:00  | Stop 1 — ANCRID  | Log in once. Show the Creator Passport at score 68. Point at the identifier. State clearly: <b>this tab stays open, we will come back to it</b> . That promise is what makes minute 14 land.                                                                                  |
| 4:00  | Stop 2 — origin  | Launch ANCRA from the launcher — no second login, and say so. The assignment, the capstone, the session that produced the work. Establishes that the work has an academic provenance no portfolio site can assert.                                                            |
| 6:00  | Stop 3 — INHEIRA | The four minutes that matter. Versions, contributions, the human-approved split sheet. Draw the distinction explicitly: <b>AI observed the contributions; humans approved the splits</b> . At 7:30, approve the split on stage. Do not narrate over the next few seconds.     |
| 10:00 | Stop 4 — value   | Switch to ANCRMEDIA: the release exists, and nobody created it. Switch to Vaulta: the royalty channel is open against that exact three-way split. Open the trace view; show one correlation ID crossing three services.                                                       |
| 13:00 | Stop 5 — close   | Return to the ANCRID tab left open at minute 2. Refresh. Score 68 → 74, new credential, registered work. Then ANCRLaunch: readiness recalculated, employer view updated. The loop is closed — verified creative work became career standing with nobody re-entering anything. |
| 15:00 | Map              | One slide, the eight applications not opened, and the architecture. Thirty seconds each on COHEIR and ANCRD; name ANCRLAB and ANCRSync as roadmap without apology. State the boundary: what was live, what was seeded.                                                        |
| 17:00 | Ask              | The specific ask, then stop talking.                                                                                                                                                                                                                                          |

## 10 Risk register

| #  | RISK                                                                                                                  | EXPOSURE           | MITIGATION                                                                                                                                                                                                                                                                                                                                                                                                |
|----|-----------------------------------------------------------------------------------------------------------------------|--------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| R1 | <b>The live event chain fails on stage.</b> The centrepiece is also the only unrehearsable part.                      | HIGH / SEVERE      | Three layers. (a) Make the chain replayable and idempotent by design — a failed publish can be re-fired without corrupting state. (b) Run the one-command reset immediately before every session. (c) Hold a screen recording of the exact same path, cued and ready; if the chain stalls for more than ten seconds, cut to it, say “here it is from this morning”, and move on without visible distress. |
| R2 | <b>“Is this real or is it seeded?”</b> asked at minute 8.                                                             | CERTAIN / MODERATE | Answer before it is asked, at minute 15. Volunteer the exact boundary — identity and the three-event chain are live, the surrounding records are demonstration data — then open the correlation trace. An unprompted, precise admission reads as engineering confidence; a defensive answer to the same question does not.                                                                                |
| R3 | <b>“What is the actual product?”</b> — the thirteen-tile problem.                                                     | LIKELY / HIGH      | Pre-empted structurally: the launcher, the single identifier and the one-thread narrative answer it before it forms. If asked anyway, the answer is one sentence — “the verified creator record; the thirteen applications are how it gets filled in.” Rehearse that sentence.                                                                                                                            |
| R4 | <b>Naming contradictions found live.</b> A URL reading ANCRSYNC on the career product, or two things called Passport. | LIKELY / HIGH      | Resolve D1 and D2 in Phase 0 and ship the UI strings as P1-H. This risk is entirely eliminable for two engineering days, and it is the kind of finding that causes an evaluator to discount everything shown afterwards.                                                                                                                                                                                  |
| R5 | <b>Demo state degrades across repeat sessions.</b> Splits already approved, scores already moved.                     | CERTAIN / MODERATE | P1-G, the one-command reset, run as a pre-session ritual rather than on demand. Snapshot every database before the first session, never after.                                                                                                                                                                                                                                                            |
| R6 | <b>An off-thread application is requested mid-demo.</b>                                                               | LIKELY / LOW       | The deferral line in section 07. Never open an unrehearsed application inside the eighteen minutes — unseeded state is where demos actually die.                                                                                                                                                                                                                                                          |
| R7 | <b>Environment drift.</b> Thirteen services, thirteen local environments, no shared configuration.                    | LIKELY / HIGH      | Bring the five thread applications under one compose file with pinned ports before the demo build starts. This is genuinely reusable infrastructure, not demo scaffolding, and it prevents the most common failure mode — a service that was running yesterday.                                                                                                                                           |
| R8 | <b>Over-promising the roadmap under questioning.</b>                                                                  | LIKELY / MODERATE  | Carry Figure 2 as a printed handout. When asked when something ships, point at the phase rather than estimating aloud. The roadmap’s credibility is an asset that survives the meeting; an off-the-cuff date is a liability that also survives the meeting.                                                                                                                                               |

### Pre-flight checklist

#### T-24 HOURS

- Database snapshot taken and reset command verified against it
- Full run-through end to end, including the event chain
- Screen recording of the successful run captured and cued
- All five thread services up under one compose file, ports pinned
- Launcher renders correctly in all five applications

#### T-15 MINUTES

- Reset run; Passport confirmed at score 68
- One clean browser profile, no other tabs, notifications silenced
- ANCRID tab opened and left open at stop 1
- Trace view pre-loaded in a background tab
- Fallback recording open in a second window, paused at 0:00



## A Appendix — canonical ownership register

One system is authoritative for each canonical record; every other product holds a reference or a projection. This table is the artefact Phase 0 must approve, and the one engineers are permitted to trust.

| PRODUCT           | QUESTION IT ANSWERS                            | CANONICAL RESPONSIBILITY                                                                            | STATUS TODAY                                          | DEMO TIER |
|-------------------|------------------------------------------------|-----------------------------------------------------------------------------------------------------|-------------------------------------------------------|-----------|
| <b>ANCRID</b>     | Who is this creator, and what may they access? | Identity, roles, institution, permissions, verification, Creator Passport, mobility, booking packet | SSO live, no consumers wired                          | CLICKED   |
| <b>ANCRA</b>      | What are they learning and achieving?          | Courses, assignments, academic progress, certificates, learning outcomes                            | Seeded persona, no auth                               | CLICKED   |
| <b>ANCRLAB</b>    | Where and how was the work created?            | Projects, studio sessions, room bookings, stems, masters, source assets                             | <b>No backend</b> — spec only                         | SHOWN     |
| <b>ANCRSync</b>   | Who are they creating with?                    | Workspaces, teams, writing rooms, shared sessions, collaboration history                            | <b>No service</b> — name currently used by ANCRLaunch | SHOWN     |
| <b>COHEIR</b>     | Who is guiding and validating their growth?    | Mentorship sessions, reviews, recommendations, cohorts, professional relationships                  | Built; local auth                                     | SHOWN     |
| <b>INHEIRA</b>    | Who contributed what, and who owns what?       | Creative evidence, versions, contributions, splits, rights, credits, publishing readiness           | Strongest domain build; local auth                    | CLICKED   |
| <b>Vaulta</b>     | What happened financially?                     | Income, expenses, contracts, invoices, grants, taxes, royalty accounting                            | Built; ecosystem data local                           | CLICKED   |
| <b>ANCRMEDIA</b>  | Where can the world experience the work?       | Presentation, channels, playback, discovery, playlists, livestream, engagement analytics            | Built; no rights or finance exchange                  | CLICKED   |
| <b>ANCRD</b>      | How does verified work become reputation?      | Professional graph, feed, communities, reputation, marketplace, events                              | Built; local users and JWT                            | SHOWN     |
| <b>ANCRLaunch</b> | What is the creator ready for next?            | Readiness, opportunities, applications, interviews, employer workflows, placements                  | Built; providers simulated from own database          | CLICKED   |

### EXTENSIONS — FIRST-CLASS PRODUCTS, NOT SYSTEMS OF RECORD

| PRODUCT              | PLACE IN THE ECOSYSTEM                                                    | BOUNDARY TO PRESERVE                                                                 | DEMO TIER       |
|----------------------|---------------------------------------------------------------------------|--------------------------------------------------------------------------------------|-----------------|
| <b>CCDP Web</b>      | Institutional site, partnership funnel, CRM, program and storefront entry | Routes into ANCR; never owns creator records                                         | HELD            |
| <b>CYNAIAH</b>       | Film, visual storytelling and emerging-media workspace                    | Creates through ANCRA/ANCRLAB contracts; hands rights to INHEIRA, media to ANCRMEDIA | OPTIONAL STOP 2 |
| <b>ANCR Passport</b> | Study abroad, cultural learning, travel readiness, global classroom       | Strictly distinct from <b>Creator Passport</b> ; always use the full name            | HELD            |

| PRODUCT  | PLACE IN THE ECOSYSTEM                                      | BOUNDARY TO PRESERVE                                                        | DEMO TIER |
|----------|-------------------------------------------------------------|-----------------------------------------------------------------------------|-----------|
| VIERATA  | Creator wellness, health and human performance              | Own permission boundary; only readiness-safe summaries may leave the module | HELD      |
| ANCRSHOP | Commerce, catalog, checkout, orders, loyalty, merchandising | Recommended single commerce system of record (decision D3)                  | HELD      |

### Definition of done — the eight interconnection tests

The ecosystem may be described as fully interconnected only when all eight hold. Phase 1 delivers tests 1 and 2 for a subset; Phase 4 delivers all eight across the estate. These are the criteria to use in place of a percentage-complete figure.

| # | TEST                                                                            | DELIVERED BY    | DEMO SHOWS             |
|---|---------------------------------------------------------------------------------|-----------------|------------------------|
| 1 | One login opens every authorised product                                        | Phase 1.3 / 3.5 | Partially — 3 of 13    |
| 2 | One <b>ancrid</b> follows the creator through every product                     | Phase 1.1       | Yes — all 13           |
| 3 | Each canonical record has exactly one declared owner                            | Phase 0         | Yes — this register    |
| 4 | Cross-product updates arrive by versioned contract, never shared database reads | Phase 2.4 / 3.3 | Partially — 3 events   |
| 5 | Files cross boundaries by immutable ID, hash and protected URL                  | Phase 3.1       | No                     |
| 6 | Revoking identity or consent propagates across all products                     | Phase 4.5       | Partially — at issue   |
| 7 | A complete audit trail explains who changed each record                         | Phase 4.4       | Partially — trace view |
| 8 | AIAH actions respect permissions and human-approval boundaries                  | Phase 4.2       | Partially — one query  |

#### RECOMMENDED DECISION

Approve the ownership register and decisions D1–D7 this week, staff the Phase 1 critical path, and set the demonstration date at week ten. The estate is further along than its integration state suggests, and the work that closes the gap is bounded, sequenced and unusually well understood for a platform at this stage.
